1st and final Bill

ಶ್ರೀ

Recorded on - 29-07-2021

M. A. R. 57 (Rule 116) No. E 483813

Measurement Book

Serial No. Drilling of Borewell and providing water facilities in ward no 13 Shettyhalli

Name of work ..... Sub division ..... From ..... To .....

Name of Contractor of nature of Agency... Hemanth Kumar S (Shree priya Enterprises)

Date of commencement of work ~~work order No~~ :- E.E./D.D./W.O./04/2020-21, Dated :- 30.01.2021 -

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
1)	~~Name of work~~ :- Geophysical investigation of site for sinking borewell for supplying drinking water It is completed as per Specification.	1	–	–	–	1 NO 1 NO	
						@ Rs. 3914.58 / NO = Rs. 3914.58	
2)	Sinking of borewell of 165mm dia clear using Super fast hydraulic rig of capacity 250 PSIG & above 900CMF It is completed as per Specification.						
	60.00 to ~~50~~ 50.00 mtr	1	–	–	50.00	50.00 mtr 50.00 mtr	
						@ Rs. 360.50 / mtr = Rs. 18024.92	

Scanned by CamScanner

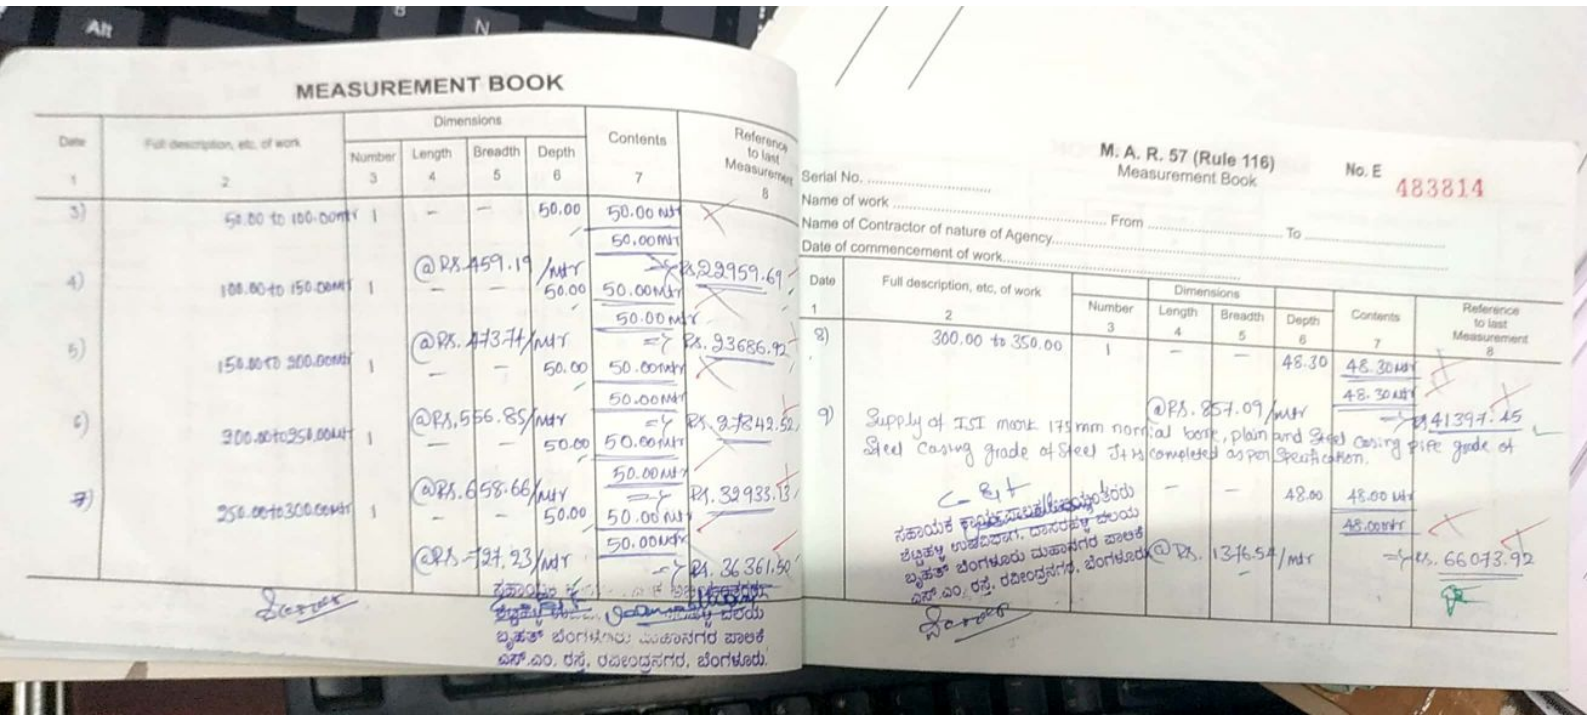

MEASUREMENT BOOK

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
3)	50.00 to 100.00 Mtr	1	–	–	50.00	50.00 Mtr	
			@ Rs. 459.19	/Mtr		50.00 Mtr	
4)	100.00 to 150.00 Mtr	1	–	–	50.00	50.00 Mtr	=Rs. 22959.69
			@ Rs. 473.71	/Mtr		50.00 Mtr	
5)	150.00 to 200.00 Mtr	1	–	–	50.00	50.00 Mtr	=Rs. 23686.92
			@ Rs. 556.85	/Mtr		50.00 Mtr	
6)	200.00 to 250.00 Mtr	1	–	–	50.00	50.00 Mtr	=Rs. 27842.52
			@ Rs. 658.66	/Mtr		50.00 Mtr	
7)	250.00 to 300.00 Mtr	1	–	–	50.00	50.00 Mtr	=Rs. 32933.13
			@ Rs. 727.23	/Mtr		50.00 Mtr	
							=Rs. 36361.50

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

M. A. R. 57 (Rule 116)
Measurement Book
No. E 483814

Serial No. .....
Name of work .....
Name of Contractor of nature of Agency..... From ..... To .....
Date of commencement of work.....

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
8)	300.00 to 350.00	1	–	–	48.30	48.30 Mtr	
						48.30 Mtr	
			@ Rs. 257.09	/Mtr			=Rs. 12413.97
9)	Supply of ISI mark 175 mm nominal bore, plain end Steel Casing grade of Steel St 34 completed as per Specification.						
	C – R/F				48.00	48.00 Mtr	
						48.00 Mtr	
			@ Rs. 1376.54	/Mtr			=Rs. 66073.92

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಚೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
15)	Supplying and drawing 3 Core PVC Sheated Submersible Pump Cable ಗಡಸುತನದ ಕೆಲಸ ಪೂರ್ಣಗೊಂಡಿದೆ as per Specification.	1	–	–	318.00	318.00 Mtr 318.00 Mtr @ ₹912.97/Mtr =₹ 290167724.46	
16)	Supply & delivery at Site brand new/Essen/Lotus/Sunsines/adars/Gr Controls best indigenous make Genuine energy Sr.M Completed as per Specification	1	–	–	–	1 NO 1 NO @ Rs. 15375.72/NO =₹ Rs. 15375.72	
17)	For providing and supplying and mounting MS box of 16 SWG Suitable for floor ಗಡಸುತನದ ಕೆಲಸ ಪೂರ್ಣಗೊಂಡಿದೆ as per Specification	1	1100.00	20.00	–	22000.00 Sq.cms	

M. A. R. 57 (Rule 116) No. E 483816
Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
						22000.00 Sq.cms	9240.00
						=₹ 2191142.32	
18)	Providing & fixing of clamps Set and borewell cap to the pump ಗಡಸುತನದ ಕೆಲಸ ಪೂರ್ಣಗೊಂಡಿದೆ as per Specification.	1	–	–	–	1 Set 1 Set @ Rs. 0.42/Sq.cms =₹ Rs. 1870.02	
19)	Supply and delivery at Site brand new best make non return valve ಗಡಸುತನದ ಕೆಲಸ ಪೂರ್ಣಗೊಂಡಿದೆ as per Specification.	1	–	–	–	1 NO 1 NO. @ Rs. 1220.71/NO =₹ Rs. 1220.71	

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
20)	Supply and delivery at site of brand new best make gate valve as per Specification.	1	-	-	-	1 NO 1 NO	
	@ Rs. 1236.29/NO					=:	Rs. 1236.29
21)	Supply and delivery at site wrought middle Steel (galvanized) 50mm GI Union. It is completed as per specification.	1	-	-	-	1 NO 1 NO	
	@ Rs. 244.14/NO					=:	Rs. 244.14
22)	Supply and delivery at site wrought middle Steel (galvanized) 50mm GI Union.	1	-	-	-	1 NO 1 NO	
	@ Rs. 181.81/NO					=:	Rs. 181.81

Recorded

Measured by

M. A. R. 57 (Rule 116) No. E 483817

Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
23)	Supply and delivery at site wrought middle Steel (galvanized) 50mm dia GI elbow. It is completed as per Specification.	1	—	—	1—	1 NO 1 NO	
	@ Rs. 181.81/NO					=:	Rs. 181, 81
24)	Labour charges for Erection, Electrification and Commissioning of pump Sets, Including aligning and balancing. It is completed as per specification.	1	—	—	—	1 Nob 1 Nob	
	@ Rs. 5869.79/Nob					=:	Rs. 5869.79

C. Supt

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶಬ್ದಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಬಾಸವರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಡಾ. ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
25)	Labour charges for Erection of Indoor type panel board and meter board Unit ftm Completed as per Specification.	1	-	-	-	1 ND 1 ND	
26)	Supplying and Fixing miniature circuit breakers/isolators on existing MCB distribution ftis Completed as per Specification. @Rs.1170.84/no	1	-	-	-	1 Each 1 Each	=₹ Rs. 1170.84
27)	Supplying and laying of L.T.U.G. Cable having aluminium Conductor pvc Insulated Sheathed ftm Completed as per Specification @Rs.1387.97/Each	35.00	-	-	-	35.00 Mtr	=₹ Rs. 1387.97

M. A. R. 57 (Rule 116)
Measurement Book

No. E 483818

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
28)	Digging of trenches of 0.6mm x 0.5 mts wide refilling the trench to the required ground level ftis completed @Rs. 155.84/Mtr	1	35.00	-	-	35.00 Mtr 35.00 Mtr	=₹ Rs. 5454.23
29)	Supplying and fixing class-A GI pipe on pole/wall/drain completed as per Specification @Rs. 348.03/Mtr	3.00	-	-	-	3.00 Mtr 3.00 Mtr	=₹ Rs. 1044.09

Cost Items

ಸಹಾಯಕ ಕಾರ್ಯ ಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ. ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

@ 348.03

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
30)	Earthing Supplying and Fixing and wiring Earth Electrode for grounding Circuits ƒ/t/s Completed as per Specification.	1	–	–	–	1 NOb 1 NOb @Rs. 3774.32/Job =Y Rs. 3774.32	
31)	Providing Supplying and fixing LT Cast iron pot heads Suitable for 1.1 KV Class UG Cable filled with necessary bitumen ƒ/t/s Completed as per Specification.	1	–	–	–	1 NO 1 NO @Rs. 516.33/NO =Y Rs. 516.33	
32)	Supplying fixing and wiring heavy duty Low Voltage Capacitors ƒ/t/s Completed as per Specification.	1	–	–	–	1 KVAR 1 KVAR @Rs. 415.56/KVAR =Y Rs. 415.56	

M. A. R. 57 (Rule 116) No. E 483819
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
33)	Supplying and fixing of polished wood board made of ply Laminate 15mm ƒ/t/s Completed as per Specification	1	–	–	–	1 Each 1 Each @Rs. 303.36/Each =Y Rs. 303.36	
34)	Earthwork Excavation for foundation of building water Supply Sanitary lines and Electrical Conduits ƒ/t/s completed as per Specification.					308.27 cum 308.27 cum @Rs. 329.27/cum =Y Rs. 101504.65	

C.E.I

ನಕಾಶೆಯ ಕಾಮಗಾರಿಗಳು ಮತ್ತು ಕಟ್ಟಡಗಳು
ಕೆಪಿಟಿಸಿಎಲ್ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಕೆಪಿಟಿಸಿಎಲ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ಕೃಷ್ಣ ಕಛೇರಿ ಸಂಕೀರ್ಣ, ಬೆಂಗಳೂರು

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
35)	Providing and Installing at Site of work P.V.C. Pipes Includes Cost of Pipe, if it is completed as per Specification.					456.70 Mtr 456.70 Mtr => Rs. 73542/-	
	P.N1: 483823/Sl.No: 35						
36)	Providing, laying, Spreading and Compacting Crushed Stone aggregates of Granite/Metal/basalt to wet mix if it is completed as per Specification.					@ Rs. 161.03/Mtr	
	P.N1: 483824/Sl.No: 36					34.25 cum 34.25 cum => Rs. 71210.20	
						@ Rs. 2079.13/cum	
37)	Providing and laying plain cement Concrete of M15 1:3:6 with OPC if it is completed as per Specification					34.25 cum 34.25 cum	
	P.N1: 483825/Sl.No: 37					@ Rs. 5723.64/cum => Rs. 196047	

Rs 7100

Veeranadham

M. A. R. 57 (Rule 116)
Measurement Book

No. E 483820

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
38)	Cement Concrete pavement construction of un-reinforced plain cement Concrete flexcrete as per Specification.					34.25 cum 34.25 cum => 190508.43	
						@ Rs. 5562.29/cum	
39)	Filling available earth around pipe lines & cable layer not exceeding 20cms in depth if it is completed as per specification.					154.135 cum 154.135 cum => 34117.78	
						@ Rs. 221.35/cum	

Veeranadham

Scanned by CamScanner

MEASUREMENT BOOK

1470384=00
1387379=00

Date	Full description, etc, of work	Dimensions				Contents	
		Number	Length	Breadth	Depth		
		3	4	5	6	7	
	Thirteen Lakhs Eighty seven thousand three hundred and seventy nine only						
	83005=00						
						Total =⟩	Rs.13,19,4
						GST Charges 12% =⟩	Rs.1583
						Grand total =⟩	Rs.14,77,4

Passed by Exe. Engineer
Asst. Engineer
BBMP Dasarahalli Division

Certificate

① The work done is satisfactorily

② There is no department issues made by Contractor

Asst Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

30/07/22

For SHREE PRIYA ENTERPRISES
Hemanthkumar S

Proprietor

Scanned by CamScanner
